Audit Tool Report Generation

1. Aramco Blockchain Material Digital Passport

Project CSM Name	Lakshanya A S
Audited Project Phases	All phases, Inception & Elobration, Transition, Inception, Construction, Construction & Transition
Auditor Name	Not Assigned
Audit Cycle	Cycle 1
Audit Date	20-02-2026

2.Overall Audit Score

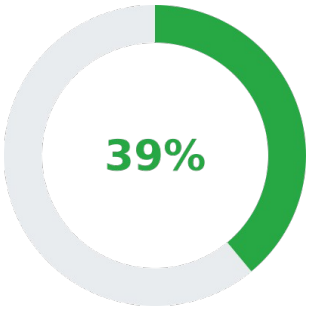

3.Health Score Breakdown

Compliance Area	Planned Score	Actual Score	Compliance Percentage
Cost	19.0	6.0	32%
Deliverable	15.0	7.5	50%

Governance	21.0	10.0	48%
Process	9.0	2.5	28%
Schedule	4.5	0.0	0%
Workdone	4.0	2.0	50%
Overall Health Score	72.5	28.0	39%

4. Non-Compliance Items:

S.No	Compliance Area	Checklist	Response	Comments
Cost				
1	Cost adherence	Is the ITD WD greater than ITD Cost?	No	Standard review completed.
2	Effort adherence	Is the Month on month cost audit performed with CSM?	No	Standard review completed.
3	Effort adherence	Is the Resource level mix (Pyramid) ratio maintained?	No	Standard review completed.
4	Effort adherence	Delivery Mandate baseline cost variance approval available for delivery mandate cost variance?	No	Standard review completed.
5	Effort adherence	Is the ITD GM% & End State GM% is greater than or equal DM GM%?	No	Standard review completed.
6	Effort adherence	Is the ITD Cost & End State Cost	No	Standard review

		is greater than or equal to Approved Cost?		completed.
Deliverable				
1	Project plan	Did the standard Project along with schedule, Milestones, deliverables shared to client?	No	Standard review completed.
2	Project plan	Did the initial Baseline dates of the plan agreed with customer?	No	Standard review completed.
3	Project plan	Did all the Milestones are aligned as per the SOW/Contract document?	No	Standard review completed.
4	Project plan	Are the Milestones aligned at the same level in the plan?	No	Standard review completed.
5	Project plan	Are the Task and Sub Tasks are mapped to the Milestone in the Plan?	No	Standard review completed.
6	Project plan	Are the Task and Sub Tasks are mapped to the deliverable in the plan?	No	Standard review completed.
7	Project Charter	Does the project charter contains all the standard sections and	No	Standard review completed.

		aligning to the contract?		
8	Sign off	Is there any overdue Sign off Observed?	No	Standard review completed.
9	Release documents	Has the Release Plan maintained and shared with client before Prod Deployment?	No	Standard review completed.
Governance				
1	Governance	Is the Plan hierarchy maintained as per standards and no deviation found?	No	Standard review completed.
2	Governance	Is the owner assignment done for all Tasks?	No	Standard review completed.
3	Governance	Are the Task status regularly updated to the Project plan?	No	Standard review completed.
4	Governance	Is the Issue log maintained and updated regularly in KTern?	No	Standard review completed.
5	Governance	Are Issue referencing done for all the Raised Issues?	No	Standard review completed.
6	Governance	Is file management properly maintained in KTern according to standards?	No	Standard review completed.

7	Governance	Are the sign offs approved with evidences on time?	No	Standard review completed.
8	Governance	Is customer participating in each weekly status meeting?	No	Standard review completed.
Process				
1	Methodology	Is the Project plan structured aligning Assurity methodology(Rational Unified Process)?	No	Standard review completed.
2	Baseline Freeze	Is the Initial Baseline Freeze done for the Project and communicated to PMO upon customer acknowledgement?	No	Standard review completed.
3	Development	Is Unit testing part of the development?	No	Standard review completed.
4	Development	Is there any dependencies impacting the project progress?	No	Standard review completed.
5	Development	Is there any blockers impacting the project progress?	No	Standard review completed.
6	Quality Assurance	Is the Training document walkthrough	No	Standard review completed.

		done to the customer?		
Schedule				
1	Schedule adherence	Is the plan is available for all the upcoming deliverables ?	No	Standard review completed.
2	Schedule adherence	Is there a release delay or delivery delay observed?	No	Standard review completed.
Workdone				
1	Workdone	Is Baseline WD lesser than or equal to Actuals WD	No	Standard review completed.

5.Audit Checklist:

http://localhost:5173/audit-execution/69980a9e434453fb743588f7?mode=view

6.Audit Report Files:

Audit_Report_Aramco Blockchain Material Digital Passport.pdf : http://localhost:5173/download-evidence?runId=69980a9e434453fb743588f7&file=Audit_Report_Aramco%20Blockchain%20Material%20Digital%20Passport.pdf
